BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Amarajothi Colony, Anjanadri Layout in ward No. 06 Thanisandra Village Limits	
2	Estimate Cost	60.00 Lakhs	
3	Administrative Approved No and Date	572/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	374/13-14, Date. 03.03.2014	
5	Job Code No. and P Code No.	006-14-000047	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	403/2013-14, Date.21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	10.06.2014	
12	Actiual Date of Completion	26.06.2014	
13	Delay if any	Nil	

14	**Reson for Delay**	Nil	
15	**Payment made till date.**	Nil	
16	**Status of Work**	Completed	
17	**Photograph verfied**	Enclosed	
18	**Date of Inspection**	16.07.2015	
19	**MB No. and Page No.**	Mb 2562 Page No.256101-117	
20	**BR No. and Date**	182/30.06.2014	
21	**Test Result**	Quality Test Report submitted by Civil Tech Consultant and Engineers is verified and Enclosed	
22	**Section officer**	Sri K Devegowda J.E	
23	**Sub Division Office**	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	**Observation**		
a	**Work Quality**	Satisfactory	
b	**Comments**	Work completed as per MB	

Executive Engineer
Byatarayanapura Division
Yelahanka Zone, B.B.M.P.
Bangalore-560092

16/07/15

Y C Kale gowda
Executive Engineer (Retd)

Amarajyothi colony

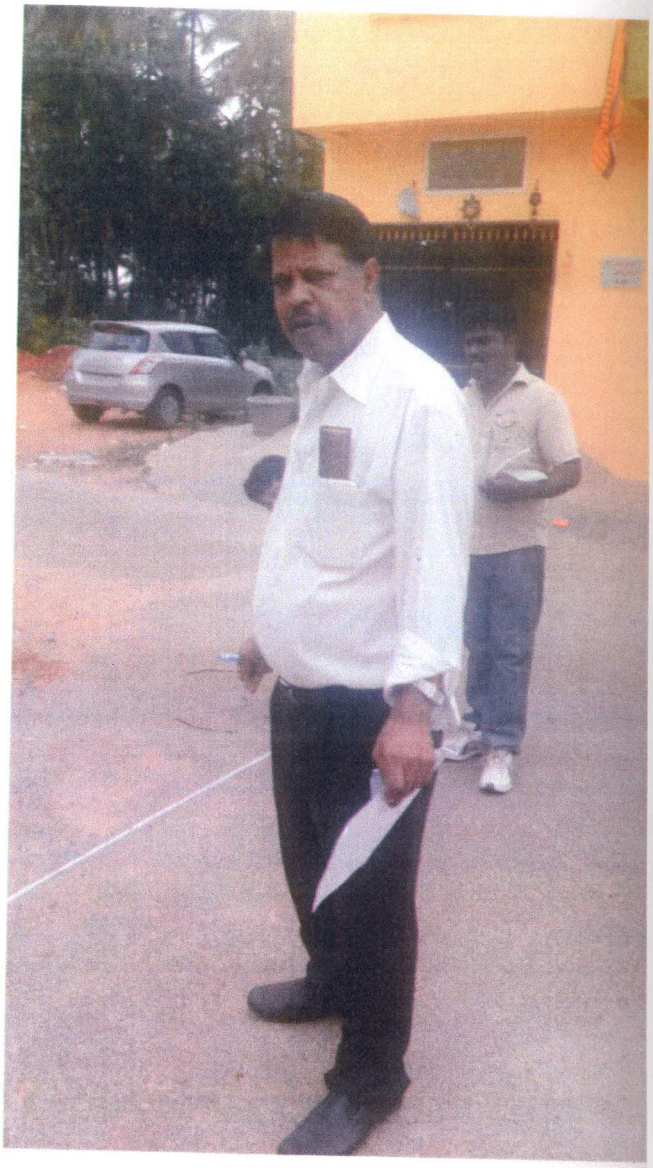

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

Amaravathi Colony

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಗ್ರಾ.ಪಂ.ರಾ. ವ್ಯವಸ್ಥೆ ಮತ್ತು ಗ್ರಾಮೀಣ ಜಲ ವಿಭಾಗ

Amaragolki Colony

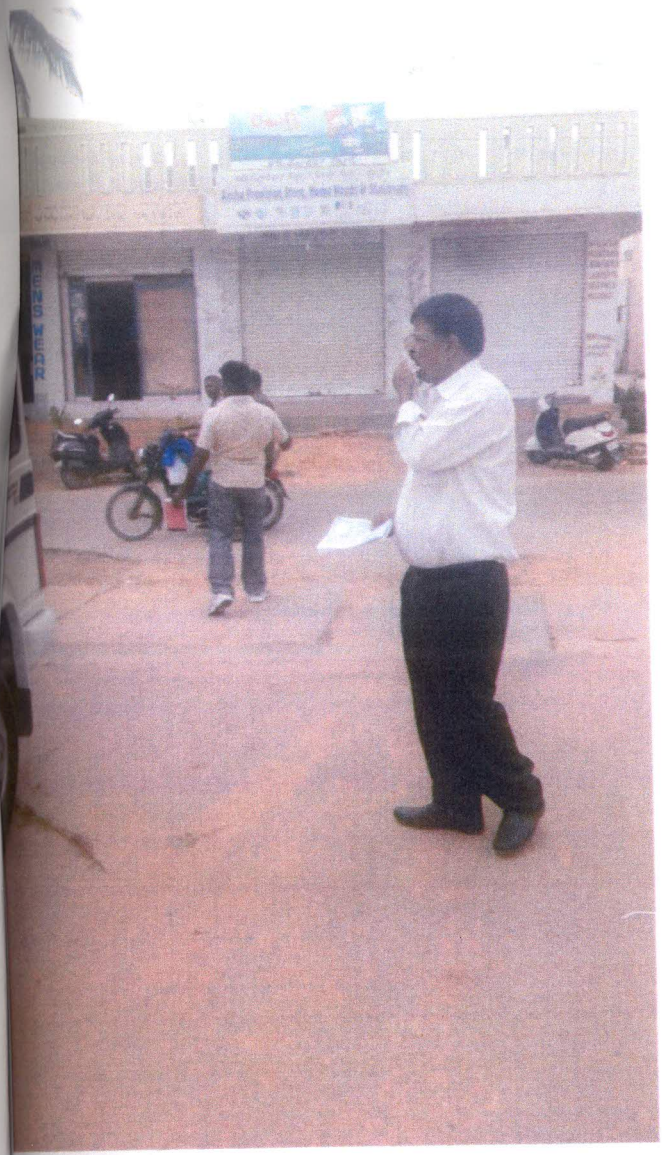

Improvements to Roads and Drains at Amarajothi Colony, Anjandri Layout in Ward No. 06 in Thanisandra Village Limits.
